This report provides an overview of the FQ3 2020/21 performance for the Commercial Services' Service.

Delivering Our Outcomes – This highlights past performance as illustrated through the Services' Key Performance Indicators

# **KEY TO SYMBOLS**

**R** Indicates the performance has not met the expected Target

**G** Indicates the performance has met or exceeded the expected Target

#### This report provides an overview of the FQ3 2020/21 performance for the Commercial Services' Service.

#### **DELIVERING OUR OUTCOMES – OUR KEY PERFORMANCE INDICATORS**

Indicator: COM113\_04-The Council's Capital Plan is delivered on time [for projects managed by the Major Projects Client Management Team] Why measure this? We can deliver major capital projects which add value to the community on time.

**Commentary:** The following Projects from the Capital Plan are being delivered by the Programme and Project Management Services team (PPMS): **1.** Oban Transit Berthing Facility (OTBF) – Closing out remaining defects: Original Forecast Completion - FQ2 FY17/18 Practical Completion Achieved – FQ2 FY17/18

Oban Maritime Visitor Facility (OMVF) – Closing out remaining defects: Original Forecast Completion – FQ4 FY16/17 Practical Completion Achieved – FQ4 FY17/18 3. Oban Public Realm Phase 1 (OPR1): Original Forecast Completion – FQ1 FY15/16 Practical Completion Achieved – FQ2 FY15/16
Oban Public Realm Phase 2 (OPR2): Main Contractor entered into Administration. Minor residual works to achieve Practical Completion are being closed out by A&BC Roads following insolvency of Main Contractor: Original Forecast Completion – FQ1 FY16/17 Revised Forecast Completion - FQ4

FY20/21


4. Rothesay Pavilion Adaptive Restoration (RPN): Main Contractor in Administration, with works 70% Complete. Replacement Contractor to be procured for works required to achieve Practical Completion. Original Forecast Completion – FQ2 FY19/20 Revised Forecast Completion – FQ3 FY21/22
5. Dunoon Queens Hall Refurbishment (DQH) – Closing out remaining of defects. Original Forecast Completion – FQ2 FY17/18 Practical Completion Achieved – FQ1 FY18/19

**6.** Helensburgh Waterfront Development (HWD) – Main Contract Awarded on 14 July 2020, construction works have commenced on site. Original Forecast Completion – FQ4 FY22/23 Revised Forecast Completion – FQ4 FY22/23


#### This indicator is now on track but to a revised plan, this is noted through the horizontal trend arrow

TARGET FQ3	ACTUAL FQ3	BENCHMARK	PERFORMANCE TREND
On Track	On Track To Revised Plan	No Benchmark	
	G		
	6		


This report provides an overview of the FQ3 2020/21 performance for the Commercial Services' Service.

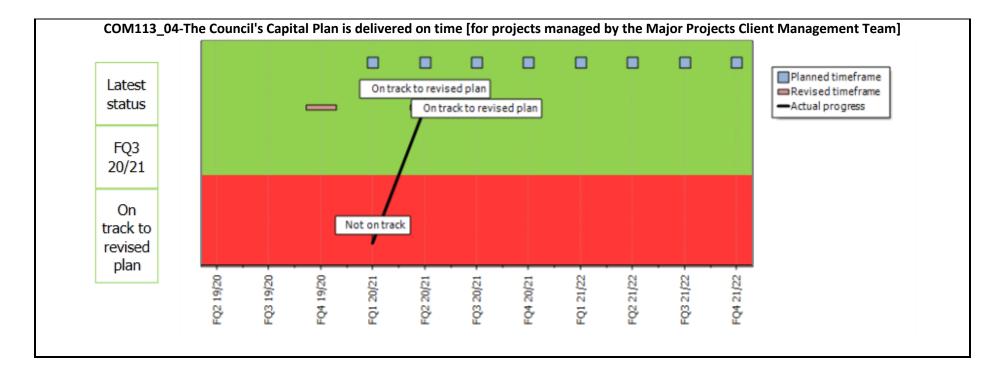

#### This report provides an overview of the FQ3 2020/21 performance for the Commercial Services' Service.

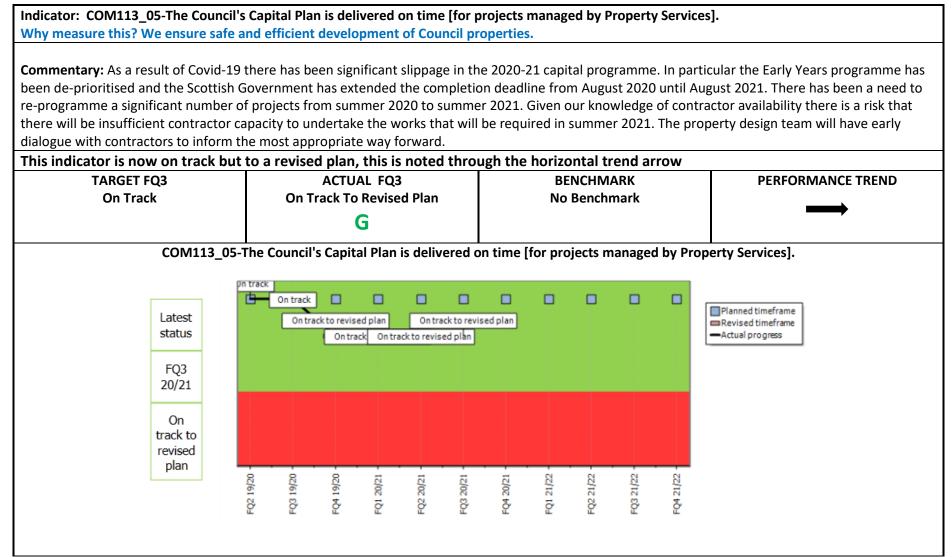

#### This report provides an overview of the FQ3 2020/21 performance for the Commercial Services' Service.

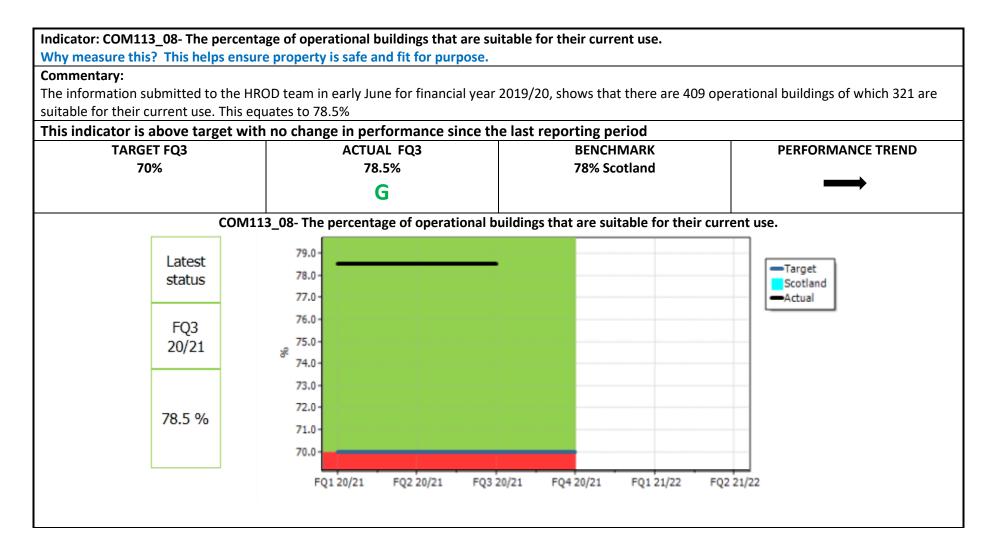

This report provides an overview of the FQ3 2020/21 performance for the Legal and Regulatory Support Service.

Delivering Our Outcomes – This highlights past performance as illustrated through the Services' Key Performance Indicators

### **KEY TO SYMBOLS**

**R** Indicates the performance has not met the expected Target

**G** Indicates the performance has met or exceeded the expected Target

